



Good Samaritan Hospital L.P.
BHCIP Funded Development Projects – Executive Dashboard
06.30.2025



Good Samaritan Hospital L.P. - BHCIP Funded Development Projects			
Project	Current Status Phase		Comments
GSH Weedpatch Clinic Integrated Wellness Clinic		Pre-Con	- B. Jones, G. Geiger had succesful zoning call with Kern County, followed up 6.26 - Onsite scheduled for 7/9 with Plant Prefab, EIR, MillerKnoll - Working with AOR to finalize specs and AOR DD Set
GSH Weedpatch Clinic Family Wellness Clinic		Design	- Will utilize same design as IWC, modular fabrication agreement signed - need final stamped set from AOR
GSH Kings County		Pre Design	- Grant awarded May 6th, 2025 - Finalized proposals, awaiting last min changes - Design Kick Off penciled for 7/10
GSH Wasco Family Clinic	??		
GSH Main Hospital Expansion		DD Lite	- GSH Plans to resubmit - EIR collected final DD sets, invoices

CONFIDENTIAL

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



GSH Weedpatch Clinics:

Integrated Wellness Center

Family Wellness Center


Overall Status	
Last Meeting	Today

Last Update: 06/23

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



Modular Clinics Production Schedule

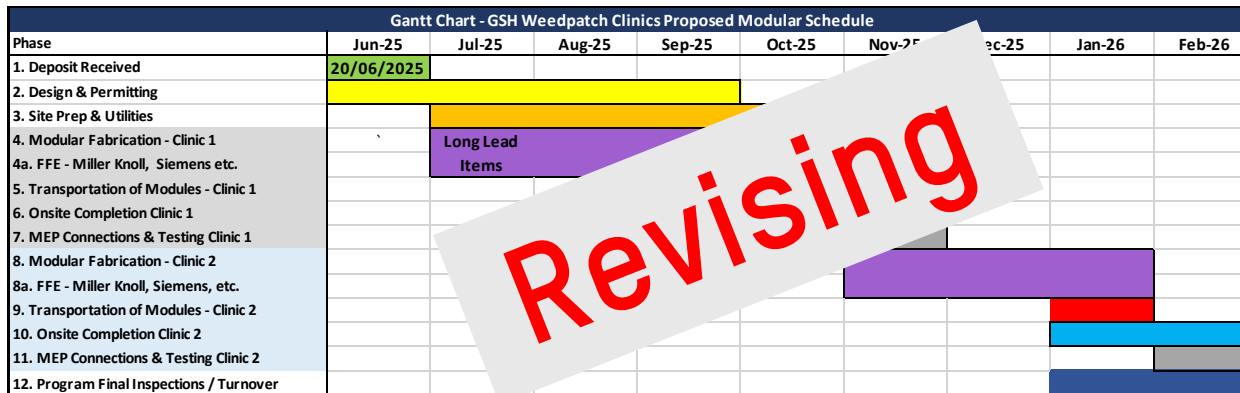

Risks / Issues / Comments

Issue: lack of engagement with AOR, design team responses

Issue: Lack of clarity around finalization of DD

Risk: On-time delivery of procurement items

Risk:

Comment: Adequate time buffer has been incorporated into the schedule for on-time delivery

Design Development Status

Feasibility	SD	DD	CD	Permits

Project Milestones

Feasibility Completed	Mar-23	
Design Process Started	Aug-23	
Engineering Teams Onboard	Aug-23	
Modular SD Phase Complete	Dec-23	
Modular DD Phase Complete	Sep-24	
CD Phase Complete		
Modular Manufacturer Report	Jul-24	
Modular Manufacturer Selected	Jul-24	
MM Engineering Agreement Signed	Apr-25	
MM Contract Signed	May-25	
GC Selected		
On-Site Work Started		
On Site Work Complete		
Site Readiness		

Key Updates

- Brian and Grant had great meeting with Kern County
 - Followed up with Craig last week; will reach out again
- Design Coordination call last week; missing engagement from AOR, CM
- Backing into design finalization with AOR 7/9
 - EIR, Plant Prefab, MillerKnoll having onsite
- Seeking design sign off from GSH team o.o.b. 7/9
- Status on GC?
- Revising production schedule on feedback from Plant Prefab; will shift

CONFIDENTIAL



GSH Kings County

Last Update: 06/23


Overall Status

Last Meeting Today

Status	Description
Off-track, no mitigation plan	
Off-track, w/ mitigation plan	
On-track	
Complete	



Proposed Project Schedule

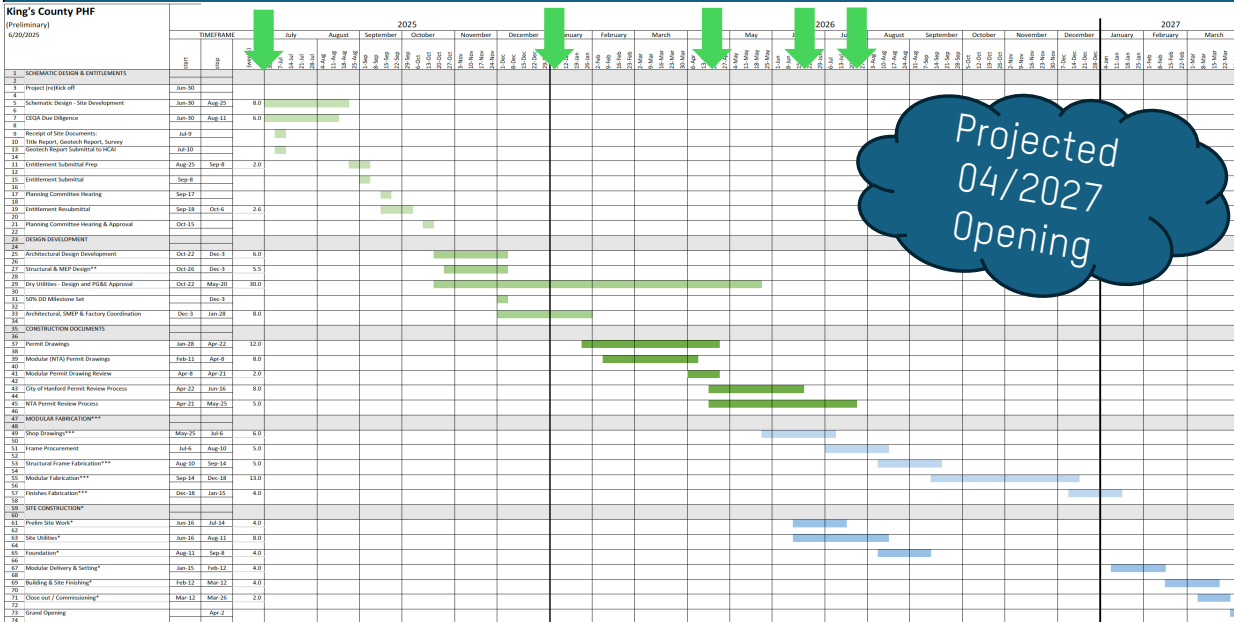

Project Schedule Notes

- Project Kick-off July 1st
- 50% DD set (Arch, MEP, Structural, Civil etc) by 12/15/2025
- Permit Set April 2026
- Site Work June 2026
- Modular Production July 2026

Design Development Status

Feasibility SD DD CD Permits

CONFIDENTIAL

Good Samaritan - Kings County Project

Design Team Proposals

Full Design Package to Construction - Stamped Drawing Sets

Name	Role	Contact	Amount	Alternate	Comments
Lowney Architecture	AOR	P. Smith	749,250.00	674,500.00	- Looking for 10% pricing adjustment (Incl. \$ credit from Dec) - Lower fee since EIR takes on some coordination - Proposal is within industry standards (~5-8%) - Received alt proposal from Darden, all in about the same
-- Green MEP	MEP & T24		40,800.00	40,800.00	- This number is low; good VE
-- HHM	Civil & Landscape		128,640.00	125,000.00	- Looking for 1-3% adjustment
Tamarack Grove	Structural EOR	W. Workman	110,000.00	110,000.00	
LPA	Program Mgmt	M. Lihony	278,600.00	125,000.00	- Scope misaligned; waiting on resubmit
EIR	Modular CM	G. Geiger	175,000.00	175,000.00	Through CD; does not include manufacturing
Sub-total			1,482,290.00	1,250,300.00	

Pushing 15% cost reduction

Key Updates

- BHCIP Award announcement 05/06/2025
- Have received final proposals from design team.
 - LPA scope misaligned; awaiting revision
 - Received alternate from Darden. Lower AOR prices but higher fees (\$341k MEP)
- Majority of design team (EIR, Lowney, TG, GSH, BHSME have aligned on **7/10 for onsite kick-off***
 - Meetings at GSH or Padre?
 - Review proposed

*assumes proposal signature beforehand



GSH Kings County

Last Update: 06/23

Overall Status	
Last Meeting	Today

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



Proposed Onsite 7/9-7/11 Schedule

EIR Healthcare			
GSH - Proposed onsite schedule July 2025			
	Wednesday, July 9th	Thursday, July 10th	Friday, July 11th
08:00			
09:00	MillerKnoll + Plant Prefab Tour and Dissucssion	GSH Kings County Kick Off Meeting	
10:00			
11:00			Kern County Planning Mtg - C. Murphy
12:00	Team Lunch	Team Lunch	
13:00			GSH Lunch
14:00	Paul Dhanens Office	GSH Kings County Kick Off	
15:00			
16:00		Kings County Planning In Person	G. Halbrook / Closeout
17:00		Kings County Site Visit	
18:00			
19:00			
20:00	EIR Team Dinner		
Notes:	1. Can Good Samaritan Host the Jul 10th kick-off? We would need conference room, lunch for aprox 8-10 ppl. Can also host at Padre Hotel. 2. Everyone free to join us for the Plant Prefab Factory tour 3. Would also like to fit in, in person meeting with Kern County 4. EIR Healthcare will host dinner 7/9 for all teams 5. Would like to have closeout lunch 7/11 with Minty, Dr Bagga?		

EIR Healthcare	
GSH - Proposed onsite schedule July 2025	
Thursday, July 10th	
08:30	- Kick off breakfast; meet and greet
09:00	Opening remarks M. Dillon, G. Geiger, B. Jones Dr. Bagga
09:15	Team Introduction: Lowney
09:30	Team Introduction: Lowney Project Spotlight
09:45	- Break -
10:00	Team Introduction: LPA
10:15	Team Introduction: LPA Project Spotlight
10:30	Team Introduction: EIR
10:45	Team Introduction: BHSME
11:00	First Break Out Session: DfMA Principles, G. Geiger
11:15	First Break Out Session: DfMA Principles, G. Geiger
11:30	Group Activity: DfMA <i>sprint</i>
11:45	Group Activity: DfMA Review
12:00	- Lunch -
12:30	Group Activity
13:00	Group Activity
13:30	Review Process Definition
14:00	Process Assignment
14:30	Kick Off Group Closeout

CONFIDENTIAL
