



Good Samaritan Hospital L.P. BHCIP Funded Development Projects – Executive Dashboard



Good Samaritan Hospital L.P. - BHCIP Funded Development Projects			
Project	Current Status Phase		Comments
GSH Weedpatch Clinic Integrated Wellness Clinic		Pre-Con	- WIC letter submitted to K. County awaiting reply and next steps - Modular DD Design Complete - Working with AOR to finalize specs and AOR DD Set - Agreement with Plant Prefab signed
GSH Weedpatch Clinic Family Wellness Clinic		Design	- Will utilize same design as IWC, modular fabrication agreement signed - need final stamped set from AOR
GSH Kings County		Pre Design	- Grant awarded May 6th, 2025 - Soliciting proposals from AEC teams; Lowney, LPA revising scope and proposals now; Have proposal from TG - Looking to kick off Design in July
GSH Wasco Family Clinic			
GSH Main Hospital Expansion		DD Lite	- GSH Plans to resubmit
GSH Baker Street			
GSH McFarland Family Clinic			UNK

CONFIDENTIAL

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



GSH Weedpatch Clinics:

Integrated Wellness Center


Family Wellness Center

Overall Status	
Last Meeting	Today
--	

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



Modular Clinics Production Schedule

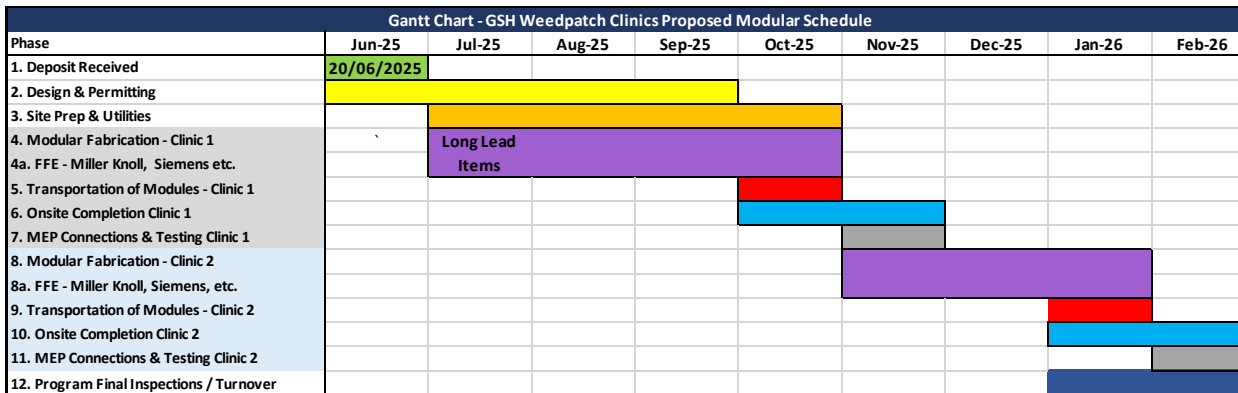

Risks / Issues / Comments

Issue: lack of engagement with AOR, design team responses

Issue: Lack of clarity around finalization of DD

Risk: On-time delivery of procurement items

Risk:

Comment: Adequate time buffer has been incorporated into the schedule for on-time delivery

Design Development Status				
Feasibility	SD	DD	CD	Permits

Project Milestones

Feasibility Completed	Mar-23	
Design Process Started	Aug-23	
Engineering Teams Onboard	Aug-23	
Modular SD Phase Complete	Dec-23	
Modular DD Phase Complete	Sep-24	
CD Phase Complete		
Modular Manufacturer Report	Jul-24	
Modular Manufacturer Selected	Jul-24	
MM Engineering Agreement Signed	Apr-25	
MM Contract Signed	May-25	
GC Selected		
On-Site Work Started		
On Site Work Complete		
Site Readiness		

Key Updates

- Modular agreement with Plant Prefab finalized; sending deposit this week
- Scheduling another design coordination call this week
- Sent letter to Kern Co Planning last week; in contact with Craig Murphy

CONFIDENTIAL



GSH Kings County

Overall Status	
Last Meeting	Today
--	

Status	Description
	Off-track, no mitigation plan
	Off-track, w/ mitigation plan
	On-track
	Complete



Modular Clinics Production Schedule

Project Milestones		
Feasibility Completed	Dec-24	
Design Process Started	Jul-25	
Engineering Teams Onboard	Jul-25	
Modular SD Phase Complete		
Modular DD Phase Complete		
CD Phase Complete		
Modular Manufacturer Report		
Modular Manufacturer Selected		
MM Engineering Agreement Signed		
MM Contract Signed		
GC Selected		
On-Site Work Started		
On Site Work Complete		
Site Readiness		

Risks / Issues / Comments

Issue:

Risk:

Comment:

Design Development Status				
Feasibility	SD	DD	CD	Permits

Key Updates

- BHCIP Award announcement 05/06/2025
- Received proposal from Lowney for AOR, and Tamarack Grove for Structural. Awaiting proposal from LPA for Design Coordn, and Program Management
